



PIEDMONT
PLANNING AND WORKING
FOR THE FUTURE
OKLAHOMA



SRB
ENGINEERING | SURVEYING | PLANNING
SMITH ROBERTS BALDISCHWILER, LLC

Water and Wastewater Improvements Progress Update to Council

10/27/2025


1

Agenda

Review Progress Made, Upcoming Activities, and Any Discussion Items

- Water Projects
 - PMA 25-001 Water Distribution System Improvements
 - PMA 25-002 1 MG Elevated Storage Tank
 - PMA 25-003 Redrill Water Wells Design Services
 - PMA 25-004 Secondary OKC Water Connection
 - PMA 25-005 Additional Water Design Services
 - PREP Grant Waterline
- Wastewater Projects
 - PMA 25-006 Sanitary Sewer Evaluation Study
 - PMA 25-007 Wastewater Master Plan and Hydraulic Model
- Schedule and Budget

2

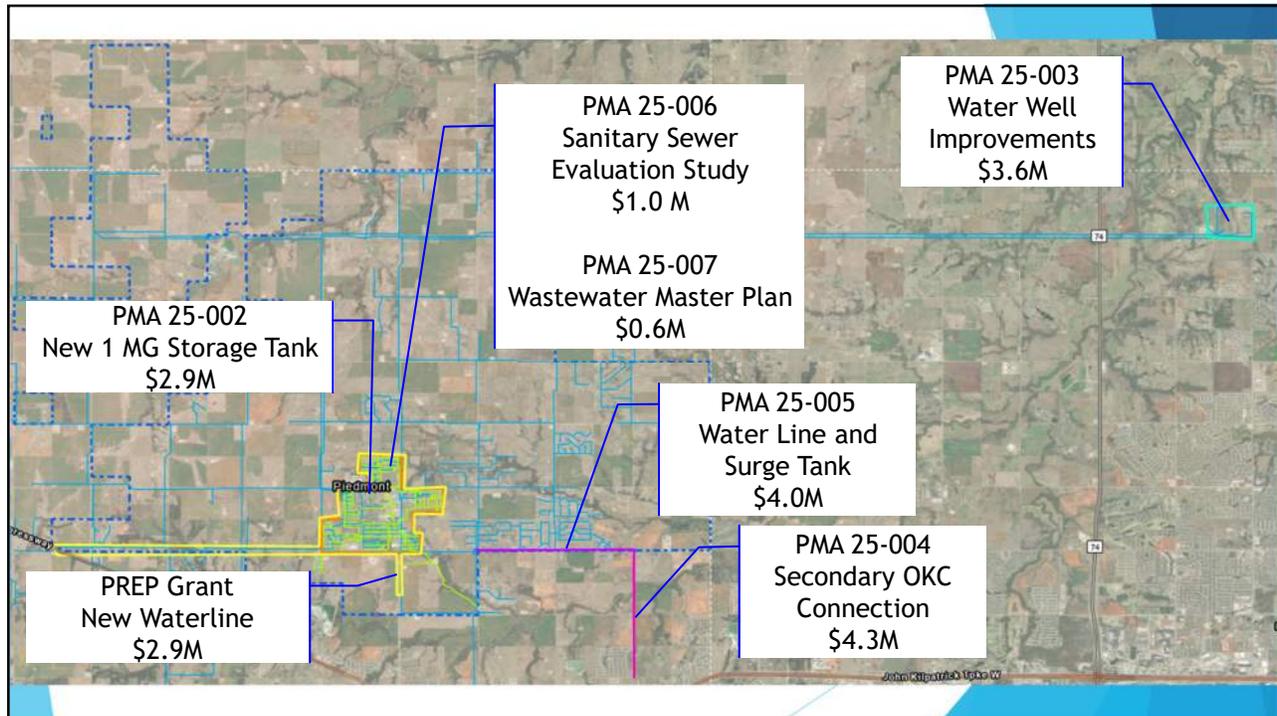

3

Water Projects

PMA	Progress Made	Upcoming	Discussion
25-001 Water Distribution Improvements	<ul style="list-style-type: none"> Completed 1 MG Tank Outlet Upgrade Received remaining flow meters 	<ul style="list-style-type: none"> Install flow meters Analyze SCADA system and valve control 	<ul style="list-style-type: none"> Completed yard piping (next slides)
25-002 1 MG Elev. Storage Tank	<ul style="list-style-type: none"> Sent offer letter 	<ul style="list-style-type: none"> Negotiate with property owners Prepare plans and specs for bid 	<ul style="list-style-type: none"> Work paused until offer is accepted
25-003 Water Wells Improvements	<ul style="list-style-type: none"> Met with hydrogeologists Researching well drilling and rehab methods 	<ul style="list-style-type: none"> Evaluating current well sites for utilization Continue researching well drilling methods Getting survey 	<ul style="list-style-type: none"> Review well sites


4

Water Projects

PMA	Progress Made	Upcoming	Discussion
25-004 Secondary OKC Water Connection	<ul style="list-style-type: none"> Completed 30% design 	<ul style="list-style-type: none"> Prepare 60% design 	<ul style="list-style-type: none"> Piedmont vault location
25-005 Additional Water Design Services	<ul style="list-style-type: none"> Sent offer letters and purchase agreement 	<ul style="list-style-type: none"> Acquire property and continue design 	
PREP Grant Waterline	<ul style="list-style-type: none"> Getting survey 	<ul style="list-style-type: none"> Receive survey 	


5

Cimarron Construction Improvements

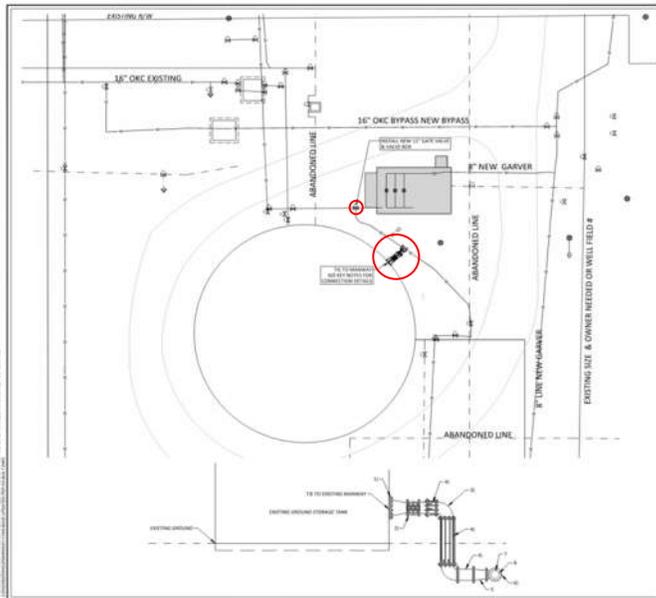


6

Current Well Sites

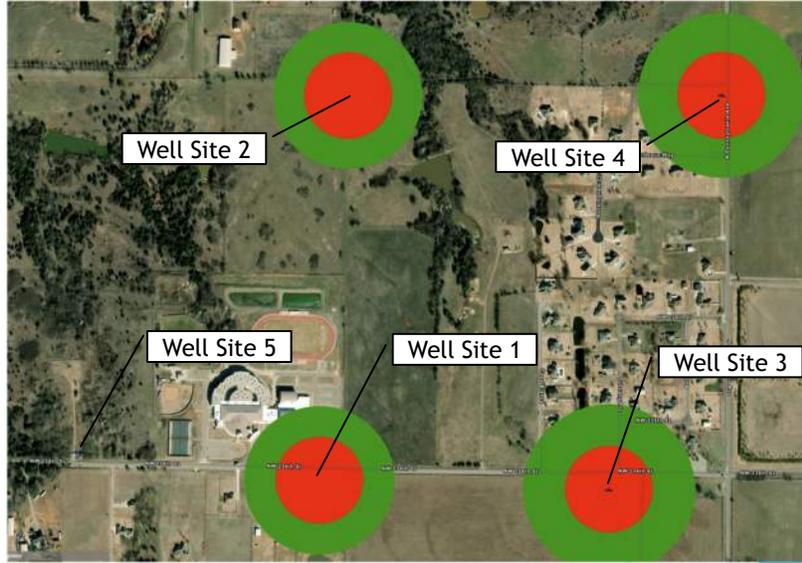

7

PMA 25-004 Waterline Upgrade Locations

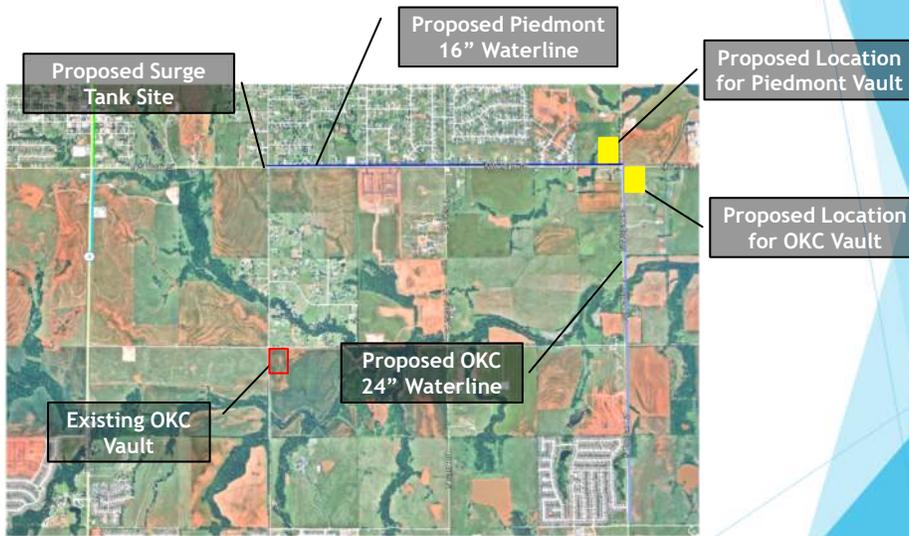


8

Wastewater Projects

PMA	Progress Made	Upcoming	Discussion
25-006 Sanitary Sewer Evaluation Study	<ul style="list-style-type: none"> Review manhole results Continued CCTV 	<ul style="list-style-type: none"> Continue CCTV Review results from manhole inspections Update GIS from manhole inspections Receive smoke testing results 	
25-007 Wastewater Master Plan & Hydraulic Model	<ul style="list-style-type: none"> Drafting report 	<ul style="list-style-type: none"> Fill in draft report 	
25-008 Wastewater Lift Station and Interceptor Improvements	<ul style="list-style-type: none"> Researching pumps for lift stations 	<ul style="list-style-type: none"> Identify pump manufacturer/model for lift stations 	

9

Schedule

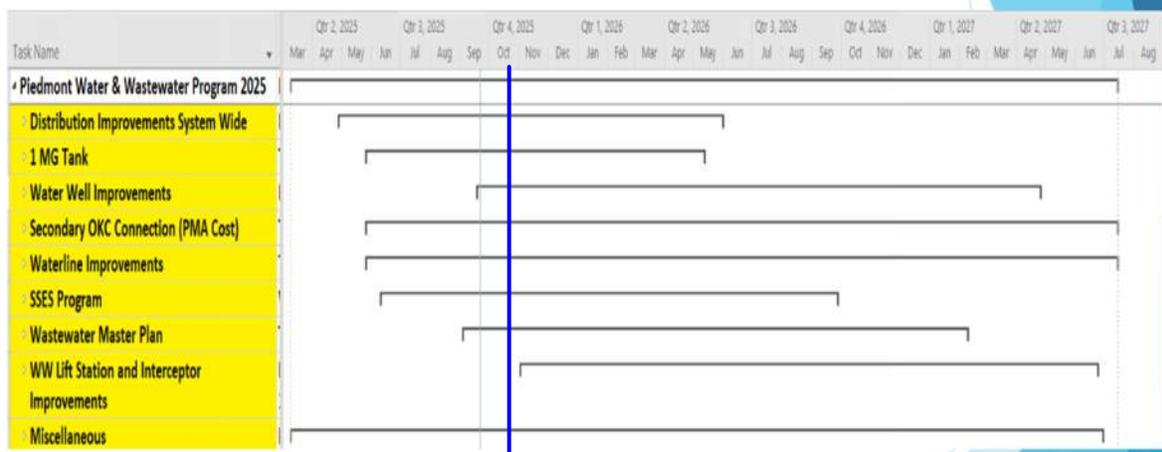

10

